


# Hunstanton Emergency Repairs Update

Dave Robson & Jade Kite

Wednesday 11<sup>th</sup> March 2026

Borough Council of  
King's Lynn &  
West Norfolk






**Area for Emergency Works  
Sections E & F**

**LEGEND**

-  SECTION DIVISIONS
-  GROYNES

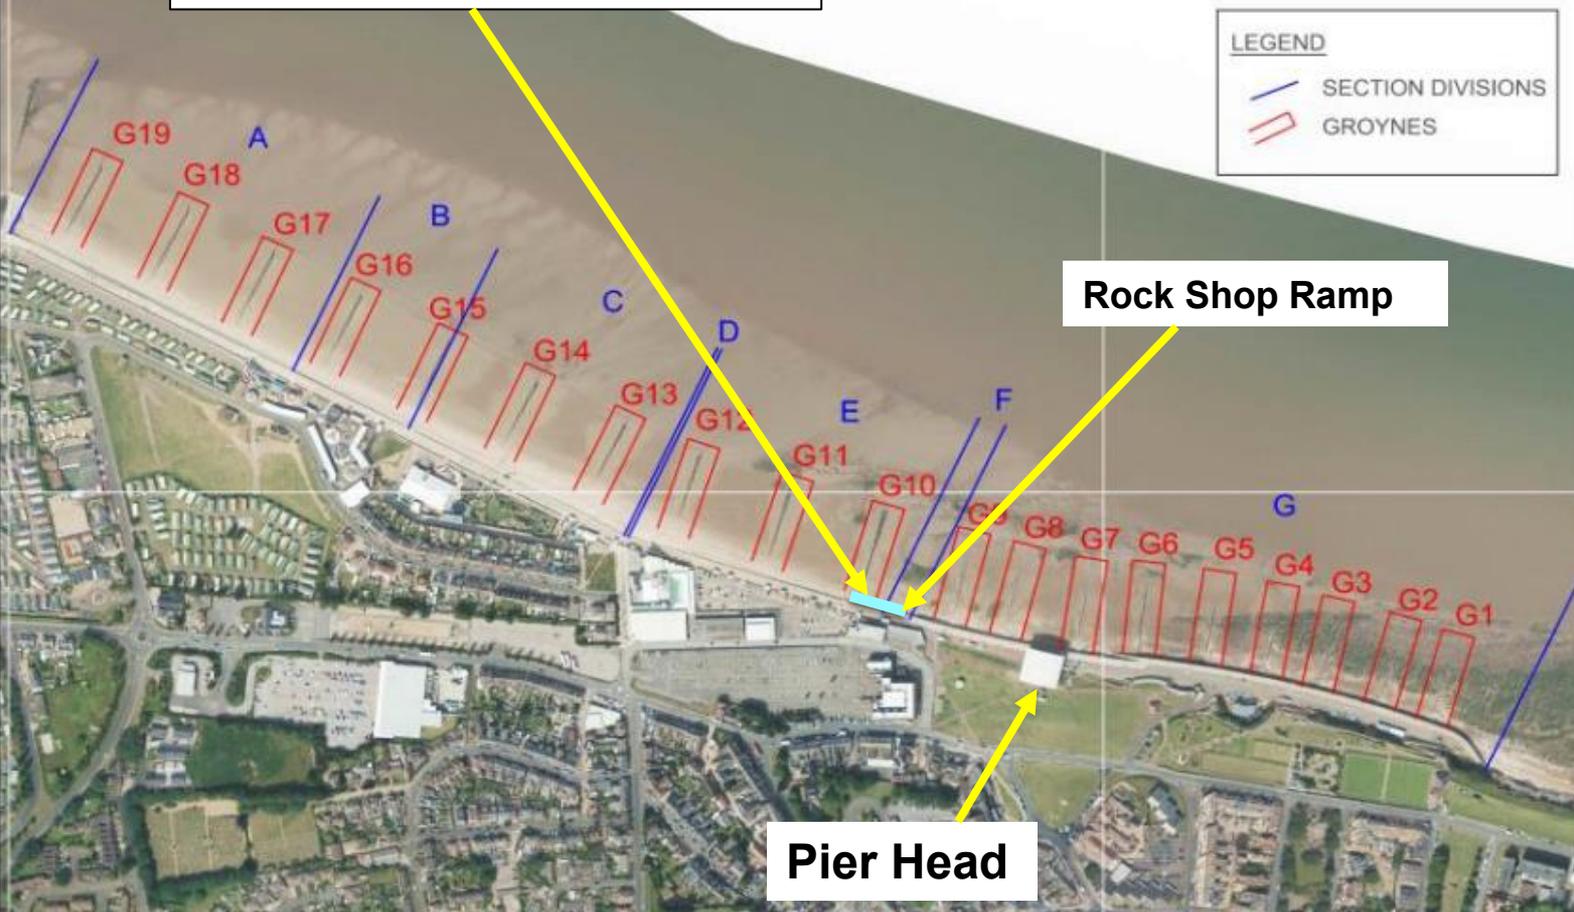

**Rock Shop Ramp**

**Pier Head**

# Expanded Site Compound

Borough Council of  
**King's Lynn &  
West Norfolk**





Site compound expanded to allow safe HGV deliveries and pedestrian access across car park.

2 traffic marshals on site to direct pedestrians, vehicles and deliveries.



# Concrete Pump & Mixer

Borough Council of  
**King's Lynn &  
West Norfolk**












# Concrete Filling

Borough Council of  
**King's Lynn &  
West Norfolk**



# Concrete fill of void



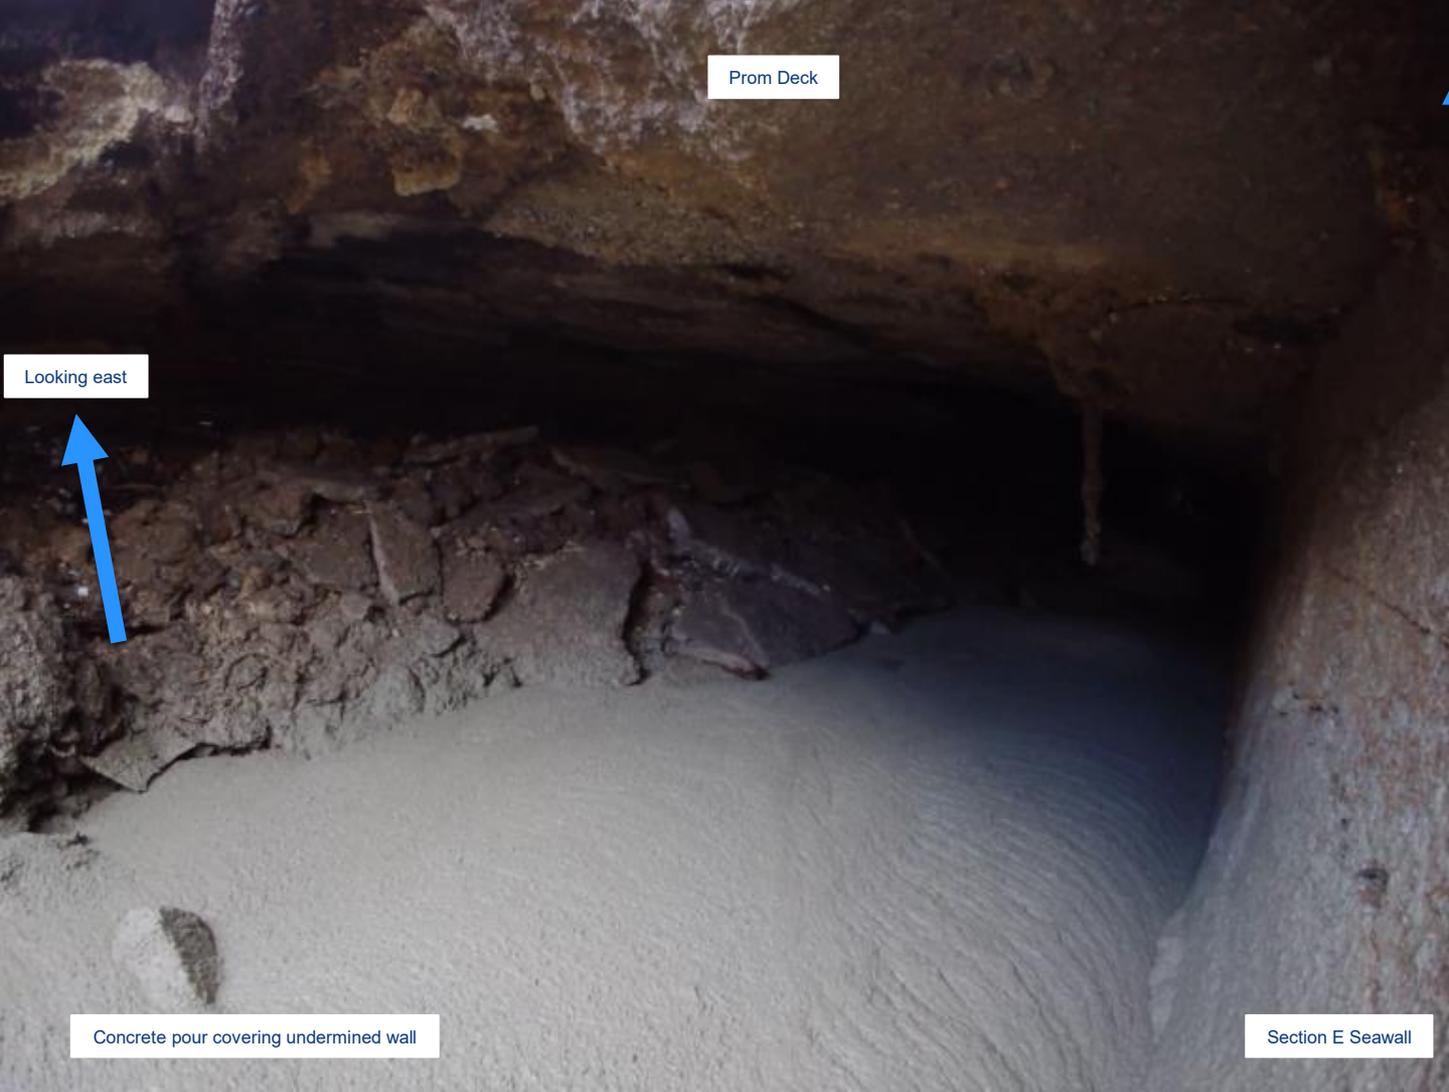

Prom Deck

Looking east



Concrete pour covering undermined wall

Section E Seawall



Looking south

Borough Council of  
King's Lynn &  
West Norfolk





Section F Seawall


Concrete pump hose

Prom Deck

Looking north

Concrete pour covering undermined wall



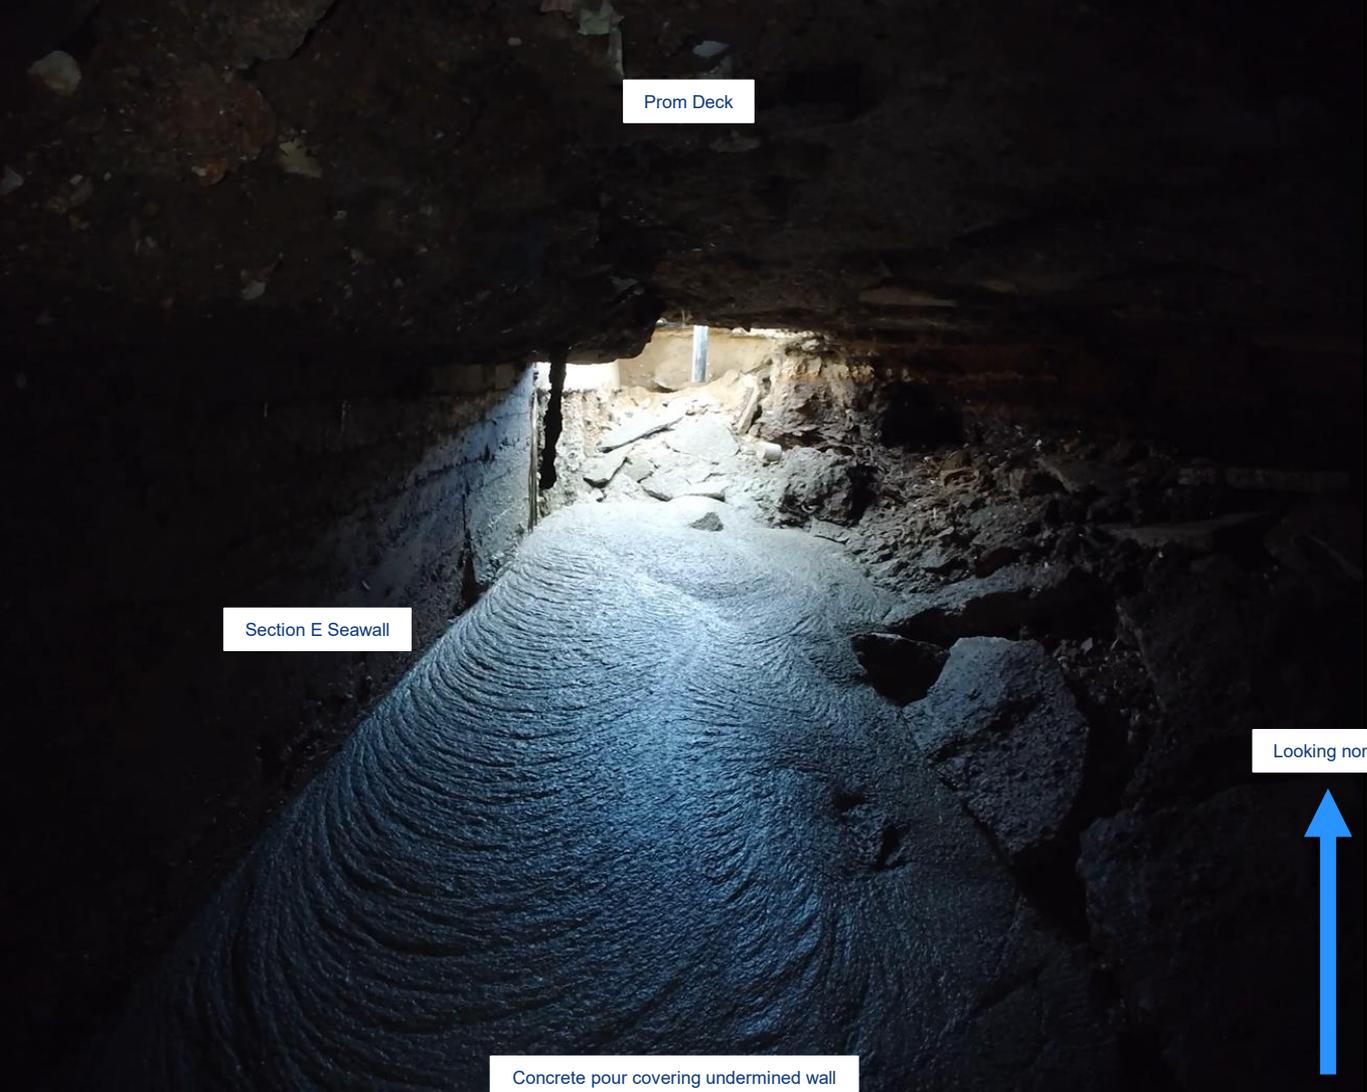

Prom Deck

Section E Seawall

Looking north

Concrete pour covering undermined wall





Prom Deck

Section E Seawall

Concrete pour covering undermined wall





Prom Deck

Section E 1920s prom slab

Section E Seawall

Concrete pour covering undermined wall

Looking south



Borough Council of  
King's Lynn &  
West Norfolk



# Next Steps

Borough Council of  
**King's Lynn &  
West Norfolk**



# Next Steps

- 3 concrete pours completed today
- 18m<sup>3</sup> of concrete poured
- Concrete pours will continue Thursday & Friday, likely into Monday
- Some weekend working – no concrete pours
- Concrete will take up to 28 days to cure and reach its designed hardness / strength

