

# Hunstanton Heritage Gardens update



The £1.3m project to refurbish and repair the areas of the Greens, Esplanade Gardens and structures along the cliff top continues to progress well, with progress evident across the site.


This project is supported by the National Lottery through the Heritage Lottery Fund and Big Lottery Fund and will be complete during June 2017.

With works continuing on the new play area and crazy golf, the Victorian shelters on cliff parade, the town sign and shelters situated around the Greens.

The new Time and Tide Garden can be seen taking shape as the focal point of the main gardens and landscape works remain on schedule.



Clockwise from top left: Works to Time and Tide Garden. New Crazy Golf: This area will be completed and opened as soon as possible once all safety surfaces and equipment is fully installed. New Rose Garden and works to Edwardian Pavilion underway : This area will soon be planted and ready to open to the public. Play area Progress: This area progresses well with one more piece of equipment to arrive before the installation of safety surface.

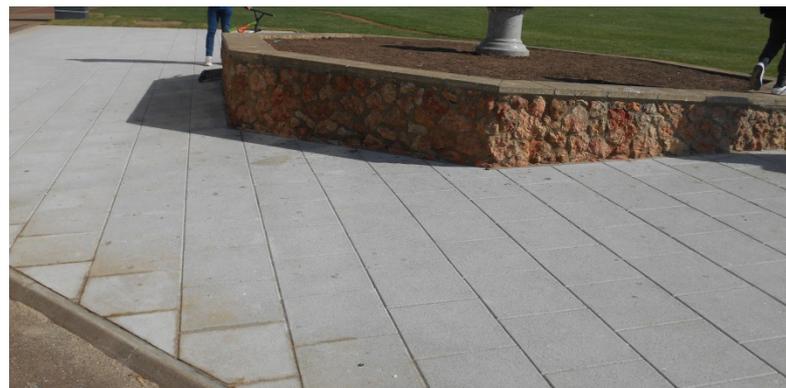

Clockwise from top left: Butterfly Shelters: Whilst progress has been hampered by conditions, the structures are now ready for refitting with their roof and panelling progress can be seen in the above photo. Lower Green area: Raised flower bed and paving to the front of the Pier building are both complete and the awaiting planting to take place. The shelter situated on the Lower Green is currently receiving its last coat of paint and the roofing is being fixed ready for the paving works to recommence.

# Next steps and Key Dates

## In the next steps are:

- Installation of safety surfacing to the play area
- Installation of the Crazy Golf equipment
- Formation of the final wall for the Time and Tide Garden
- Wood work to Butterfly shelters
- Resurfacing of the Greens pathways



Borough Council of  
King's Lynn &  
West Norfolk

